




SITE REPORT

CLARK AVENUE MIDDLE SCHOOL

DATE:	Friday, July 01, 2016	TIME:	12:00PM	BY:	Chet Osborn
WEATHER:	Sunny	TEMP:	80 F	PERMIT:	15-451 B
INSPECTIONS: 4 th floor rough electrical, CPD (3 for Verizon)					
GENERAL NOTES: Work continues throughout the building. Verizon installed pole on Tudor St., mason unable to work on Tudor but continuing with acid wash.					

#	DIV	PIC	CONTRACTOR	WORKERS	EQUIPMENT	WORK IN PROGRESS
1	00	7,8	Pinck & Co, Inc.	1		Owners representative
2	01		WTR	4		General Contractor
3	04		Fernandes	2		North veneer acid wash
3	06		Dynamic	4		4 th floor, LL
4	08	6	A&A Windows	7		Glazing South-East end of building
5	09	5	Chapman	1		4 th floor
6	09	4	West	3		1 st floor hall
7	09	3	Bello	2		3 rd floor finish coats
8	09	1	Component	17		Taping on LL & 3, hanging 4
9	09		Central Ceilings	1		1 st floor grid
10	22		Amanti	2		Rough LL
11	23		American	5		LL, 4 th floor ductwork
12	23		Harold	0		Not on site
13	26	2	YES	15		4 th floor
14	26		J&M	3		4 th floor
15	26		O'Brien	3		LL

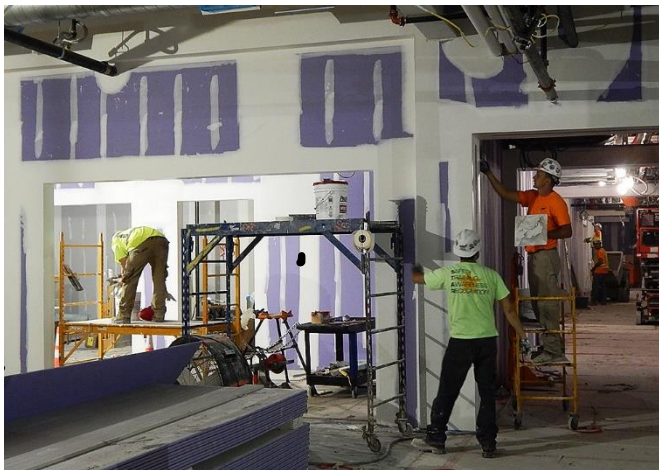

1) Taping on LL



2) Electrical inspection 4th floor



3) :Painting Room 319



4) 1st floor tile in corridor



5) Caulking windows east end 1st floor



6) Installing 3rd floor windows



7) Verizon installing pole on Tudor



8) View from the roof 7/1/16
